


(Schedule set for a 70 day process for Public Hearing and a 15 day process for Willingness Held with no Public Hearing Required)

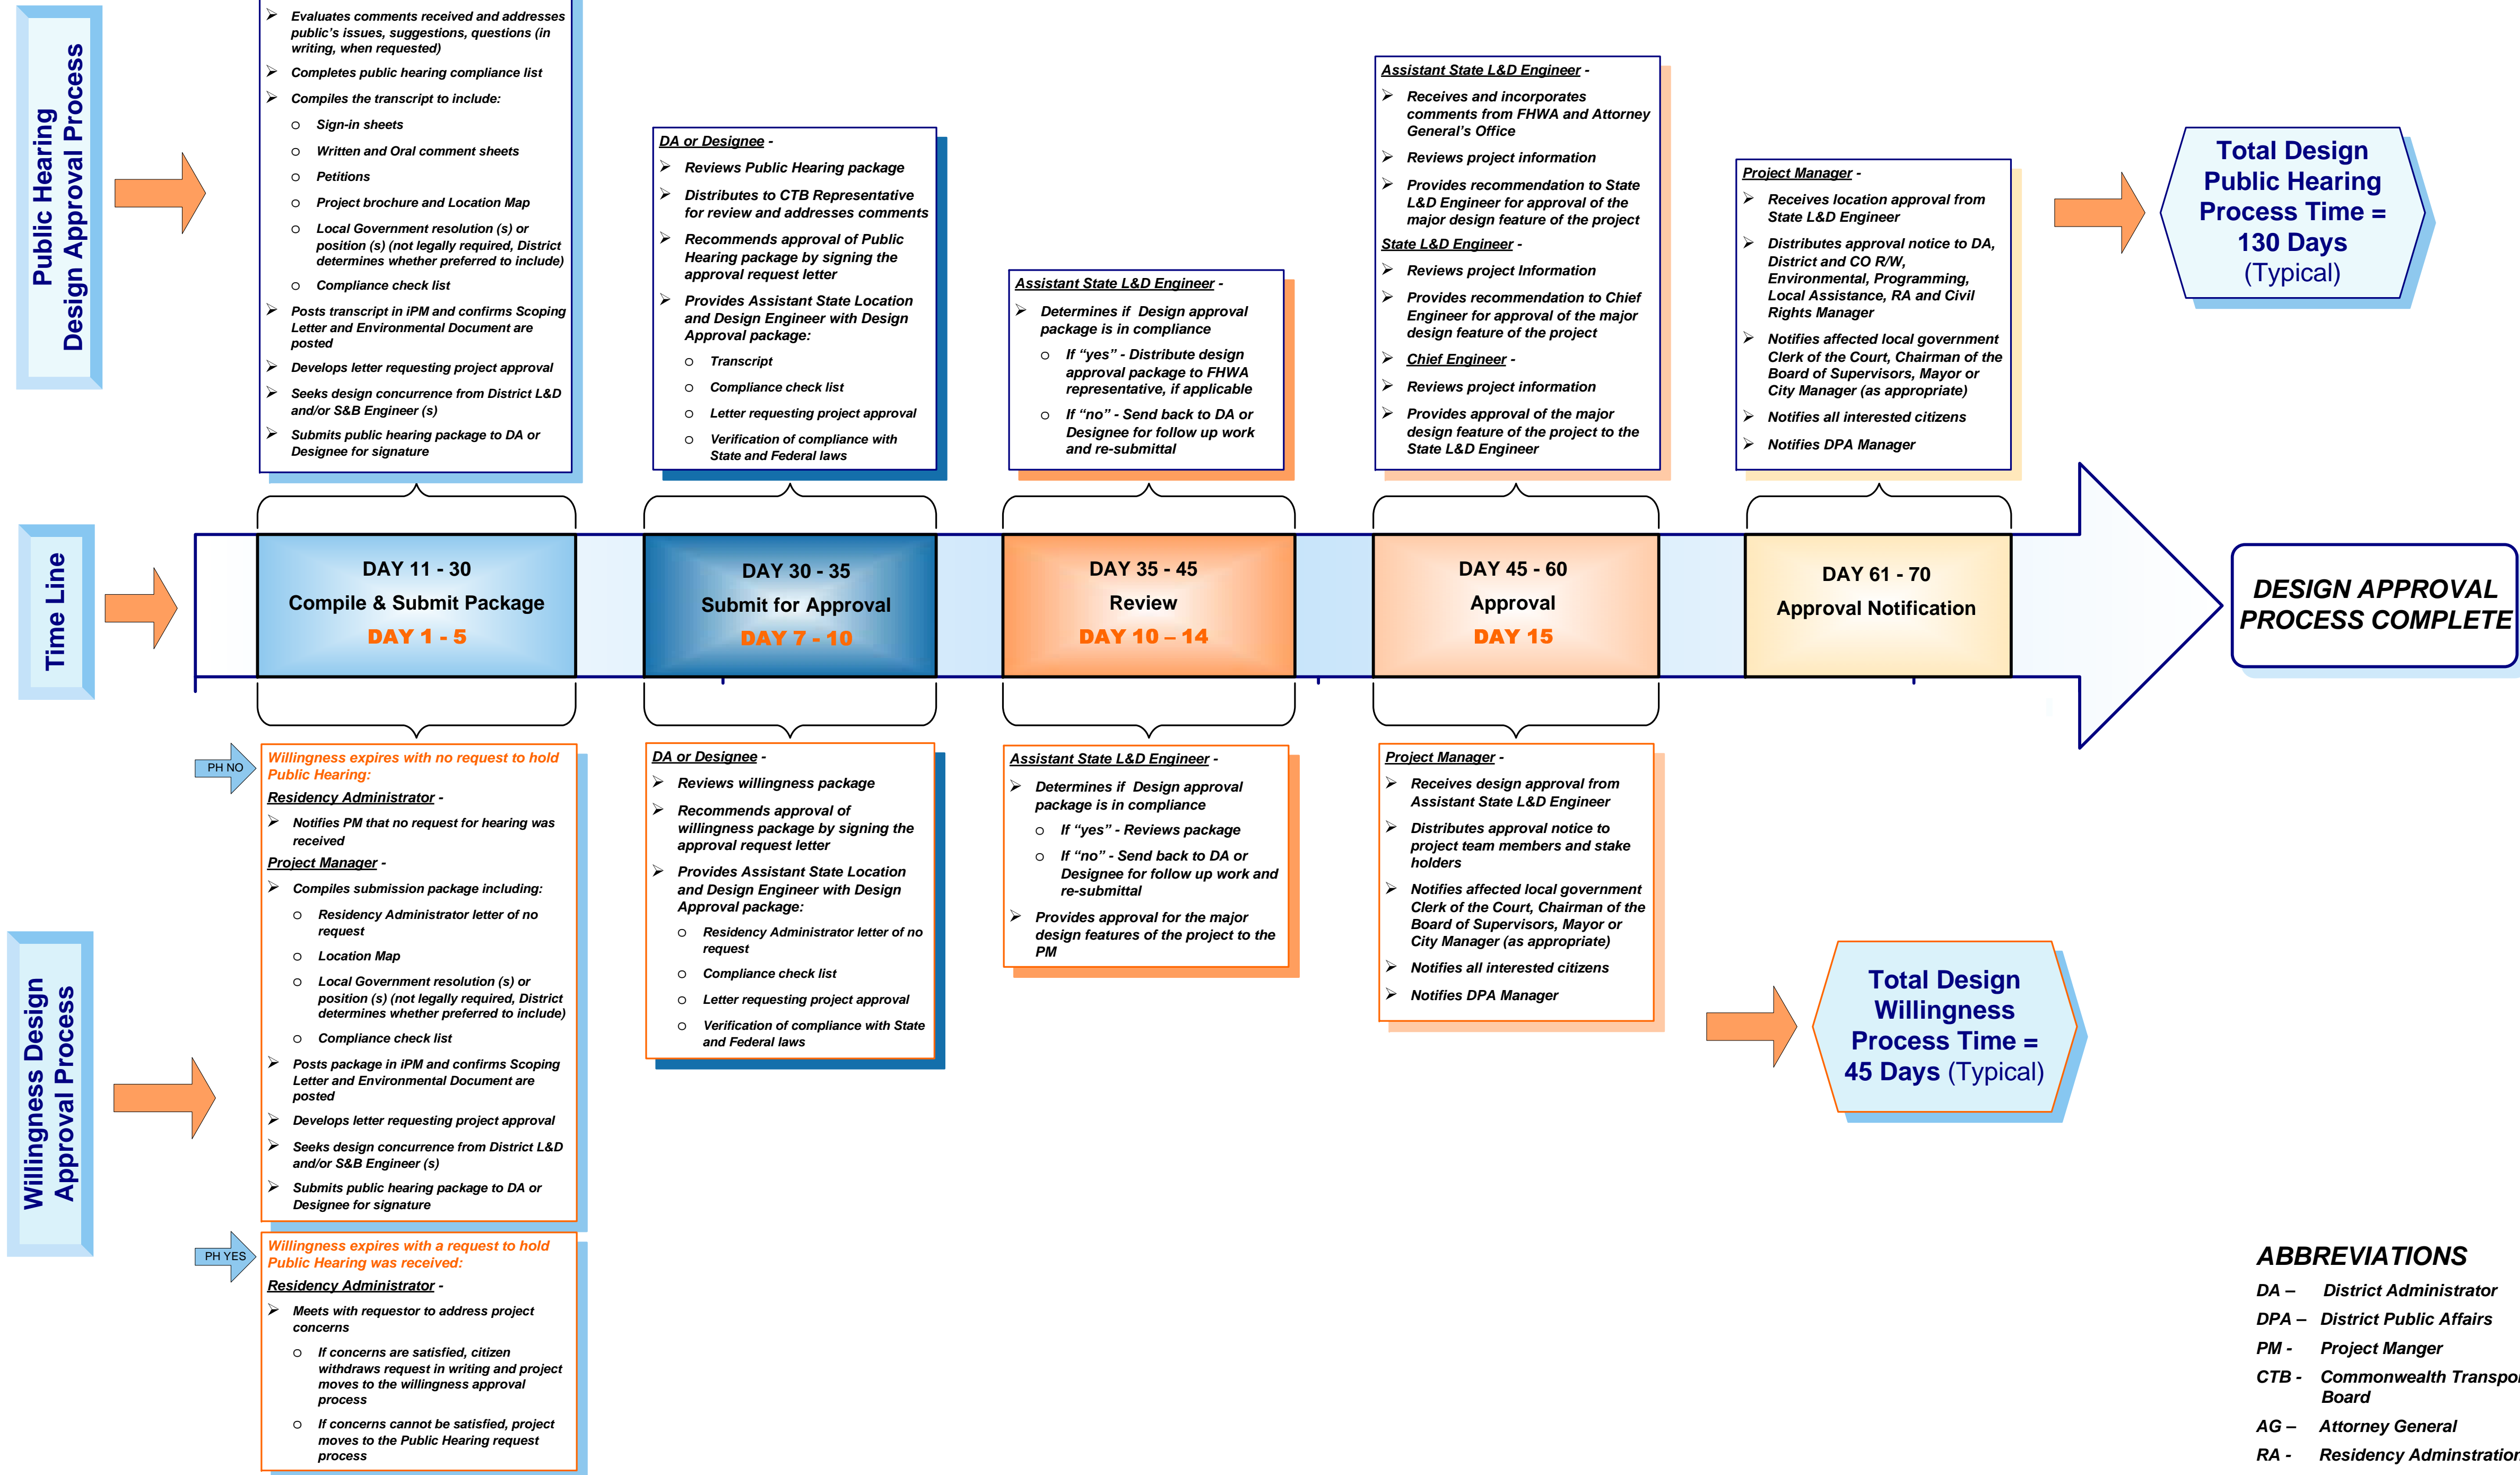

**After 10 Day comment period expires:**

**Project Manager -**

- Evaluates comments received and addresses public's issues, suggestions, questions (in writing, when requested)
- Completes public hearing compliance list
- Compiles the transcript to include:
  - Sign-in sheets
  - Written and Oral comment sheets
  - Petitions
  - Project brochure and Location Map
  - Local Government resolution (s) or position (s) (not legally required, District determines whether preferred to include)
  - Compliance check list
- Posts transcript in iPM and confirms Scoping Letter and Environmental Document are posted
- Develops letter requesting project approval
- Seeks design concurrence from District L&D and/or S&B Engineer (s)
- Submits public hearing package to DA or Designee for signature

**DA or Designee -**

- Reviews Public Hearing package
- Distributes to CTB Representative for review and addresses comments
- Recommends approval of Public Hearing package by signing the approval request letter
- Provides Assistant State Location and Design Engineer with Design Approval package:
  - Transcript
  - Compliance check list
  - Letter requesting project approval
  - Verification of compliance with State and Federal laws

**Assistant State L&D Engineer -**

- Determines if Design approval package is in compliance
  - If "yes" - Distribute design approval package to FHWA representative, if applicable
  - If "no" - Send back to DA or Designee for follow up work and re-submittal

**Assistant State L&D Engineer -**

- Receives and incorporates comments from FHWA and Attorney General's Office
- Reviews project information
- Provides recommendation to State L&D Engineer for approval of the major design feature of the project

**State L&D Engineer -**

- Reviews project Information
- Provides recommendation to Chief Engineer for approval of the major design feature of the project
- Chief Engineer -**
- Reviews project information
- Provides approval of the major design feature of the project to the State L&D Engineer

**Project Manager -**

- Receives location approval from State L&D Engineer
- Distributes approval notice to DA, District and CO R/W, Environmental, Programming, Local Assistance, RA and Civil Rights Manager
- Notifies affected local government Clerk of the Court, Chairman of the Board of Supervisors, Mayor or City Manager (as appropriate)
- Notifies all interested citizens
- Notifies DPA Manager

**DAY 11 - 30**  
**Compile & Submit Package**  
**DAY 1 - 5**

**DAY 30 - 35**  
**Submit for Approval**  
**DAY 7 - 10**

**DAY 35 - 45**  
**Review**  
**DAY 10 - 14**

**DAY 45 - 60**  
**Approval**  
**DAY 15**

**DAY 61 - 70**  
**Approval Notification**

**PH NO**

**Willingness expires with no request to hold Public Hearing:**

**Residency Administrator -**

- Notifies PM that no request for hearing was received

**Project Manager -**

- Compiles submission package including:
  - Residency Administrator letter of no request
  - Location Map
  - Local Government resolution (s) or position (s) (not legally required, District determines whether preferred to include)
  - Compliance check list
- Posts package in iPM and confirms Scoping Letter and Environmental Document are posted
- Develops letter requesting project approval
- Seeks design concurrence from District L&D and/or S&B Engineer (s)
- Submits public hearing package to DA or Designee for signature

**DA or Designee -**

- Reviews willingness package
- Recommends approval of willingness package by signing the approval request letter
- Provides Assistant State Location and Design Engineer with Design Approval package:
  - Residency Administrator letter of no request
  - Compliance check list
  - Letter requesting project approval
  - Verification of compliance with State and Federal laws

**Assistant State L&D Engineer -**

- Determines if Design approval package is in compliance
  - If "yes" - Reviews package
  - If "no" - Send back to DA or Designee for follow up work and re-submittal
- Provides approval for the major design features of the project to the PM

**Project Manager -**

- Receives design approval from Assistant State L&D Engineer
- Distributes approval notice to project team members and stake holders
- Notifies affected local government Clerk of the Court, Chairman of the Board of Supervisors, Mayor or City Manager (as appropriate)
- Notifies all interested citizens
- Notifies DPA Manager

**PH YES**

**Willingness expires with a request to hold Public Hearing was received:**

**Residency Administrator -**

- Meets with requestor to address project concerns
  - If concerns are satisfied, citizen withdraws request in writing and project moves to the willingness approval process
  - If concerns cannot be satisfied, project moves to the Public Hearing request process
